
eco BRICK Innovio

Production Line Concept

Process flow + engineering layout for the continuous eco BRICK line




Optional screening remains a side-line, not a permanent bottleneck.

Prepared as a working concept for equipment discussions, supplier RFQs, and internal layout decisions.

1. Process Flow - Updated Production Logic

eco BRICK Innovio

Continuous feed, direct cooling, direct crushing and Big Bag collection.

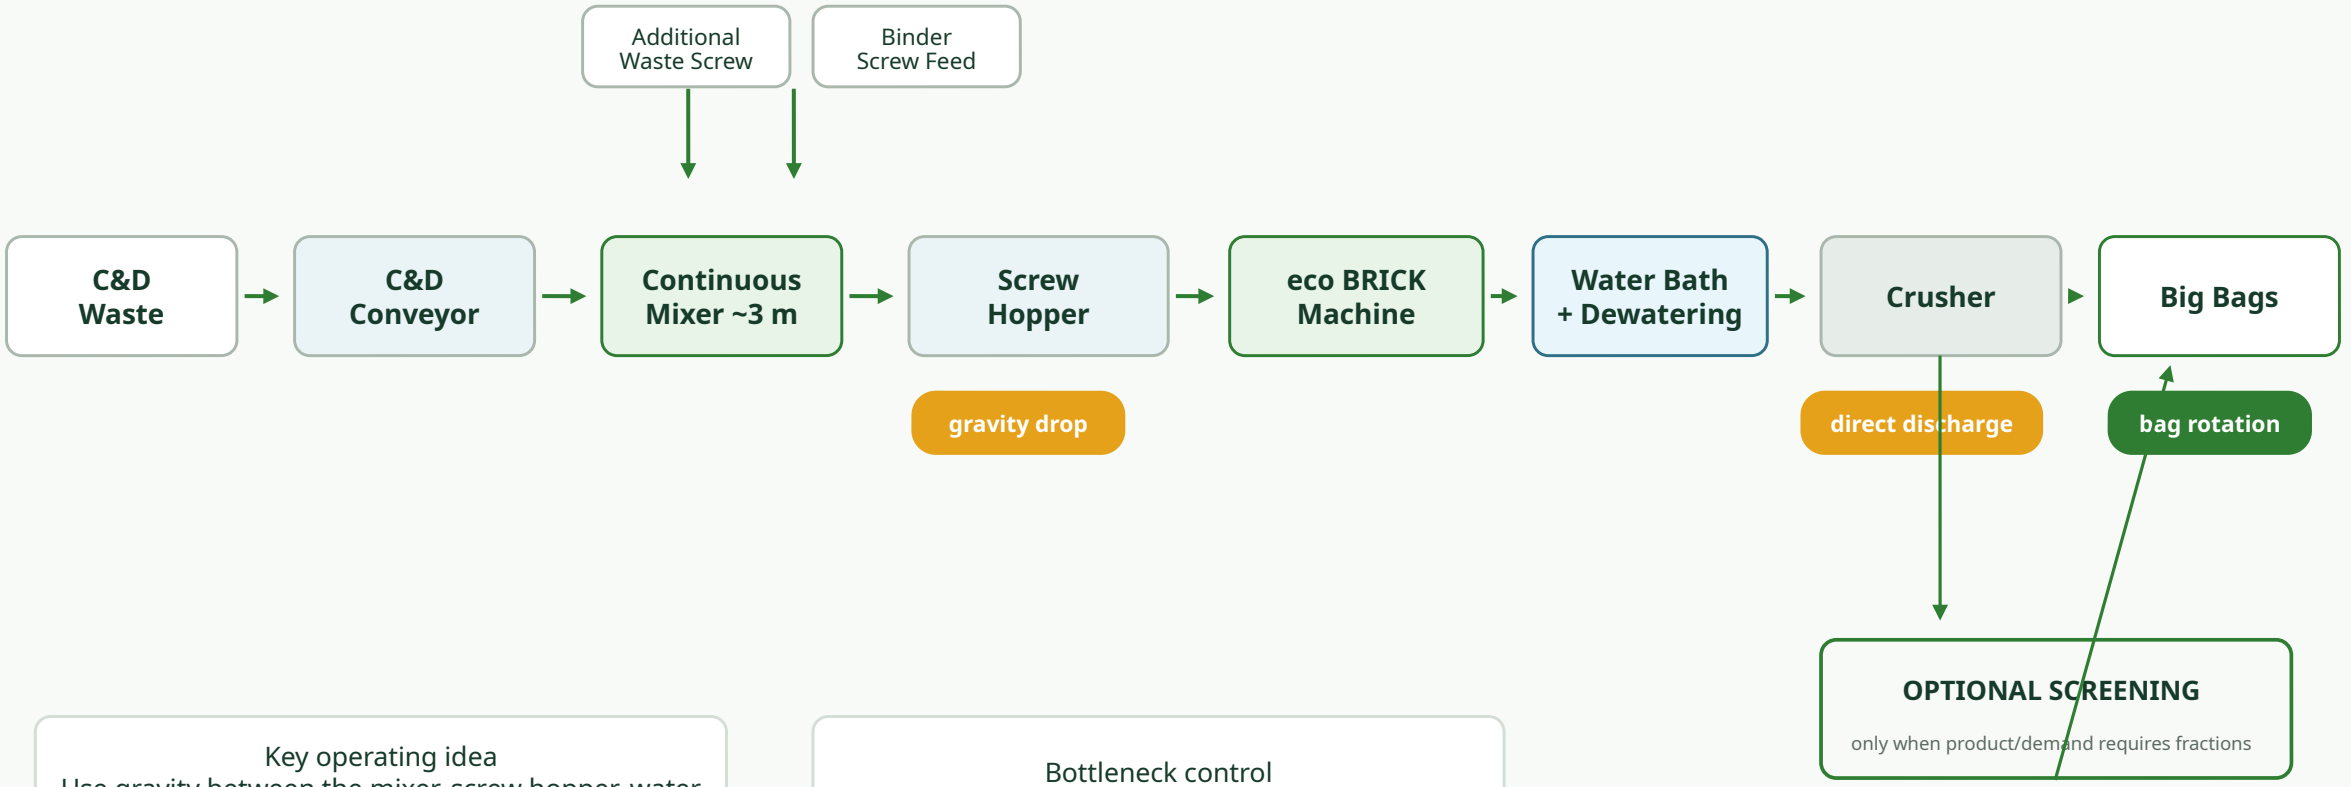


Key operating idea
Use gravity between the mixer, screw hopper, water bath/dewatering screw, and crusher wherever possible.

Bottleneck control
Screening is designed as a side-line/bypass and not as a permanent process step.

Conceptual engineering visualization - dimensions to be validated with equipment suppliers

2. Engineering Layout - Top View Concept

The core line is kept short and mostly linear. Dimensions are conceptual except where noted.

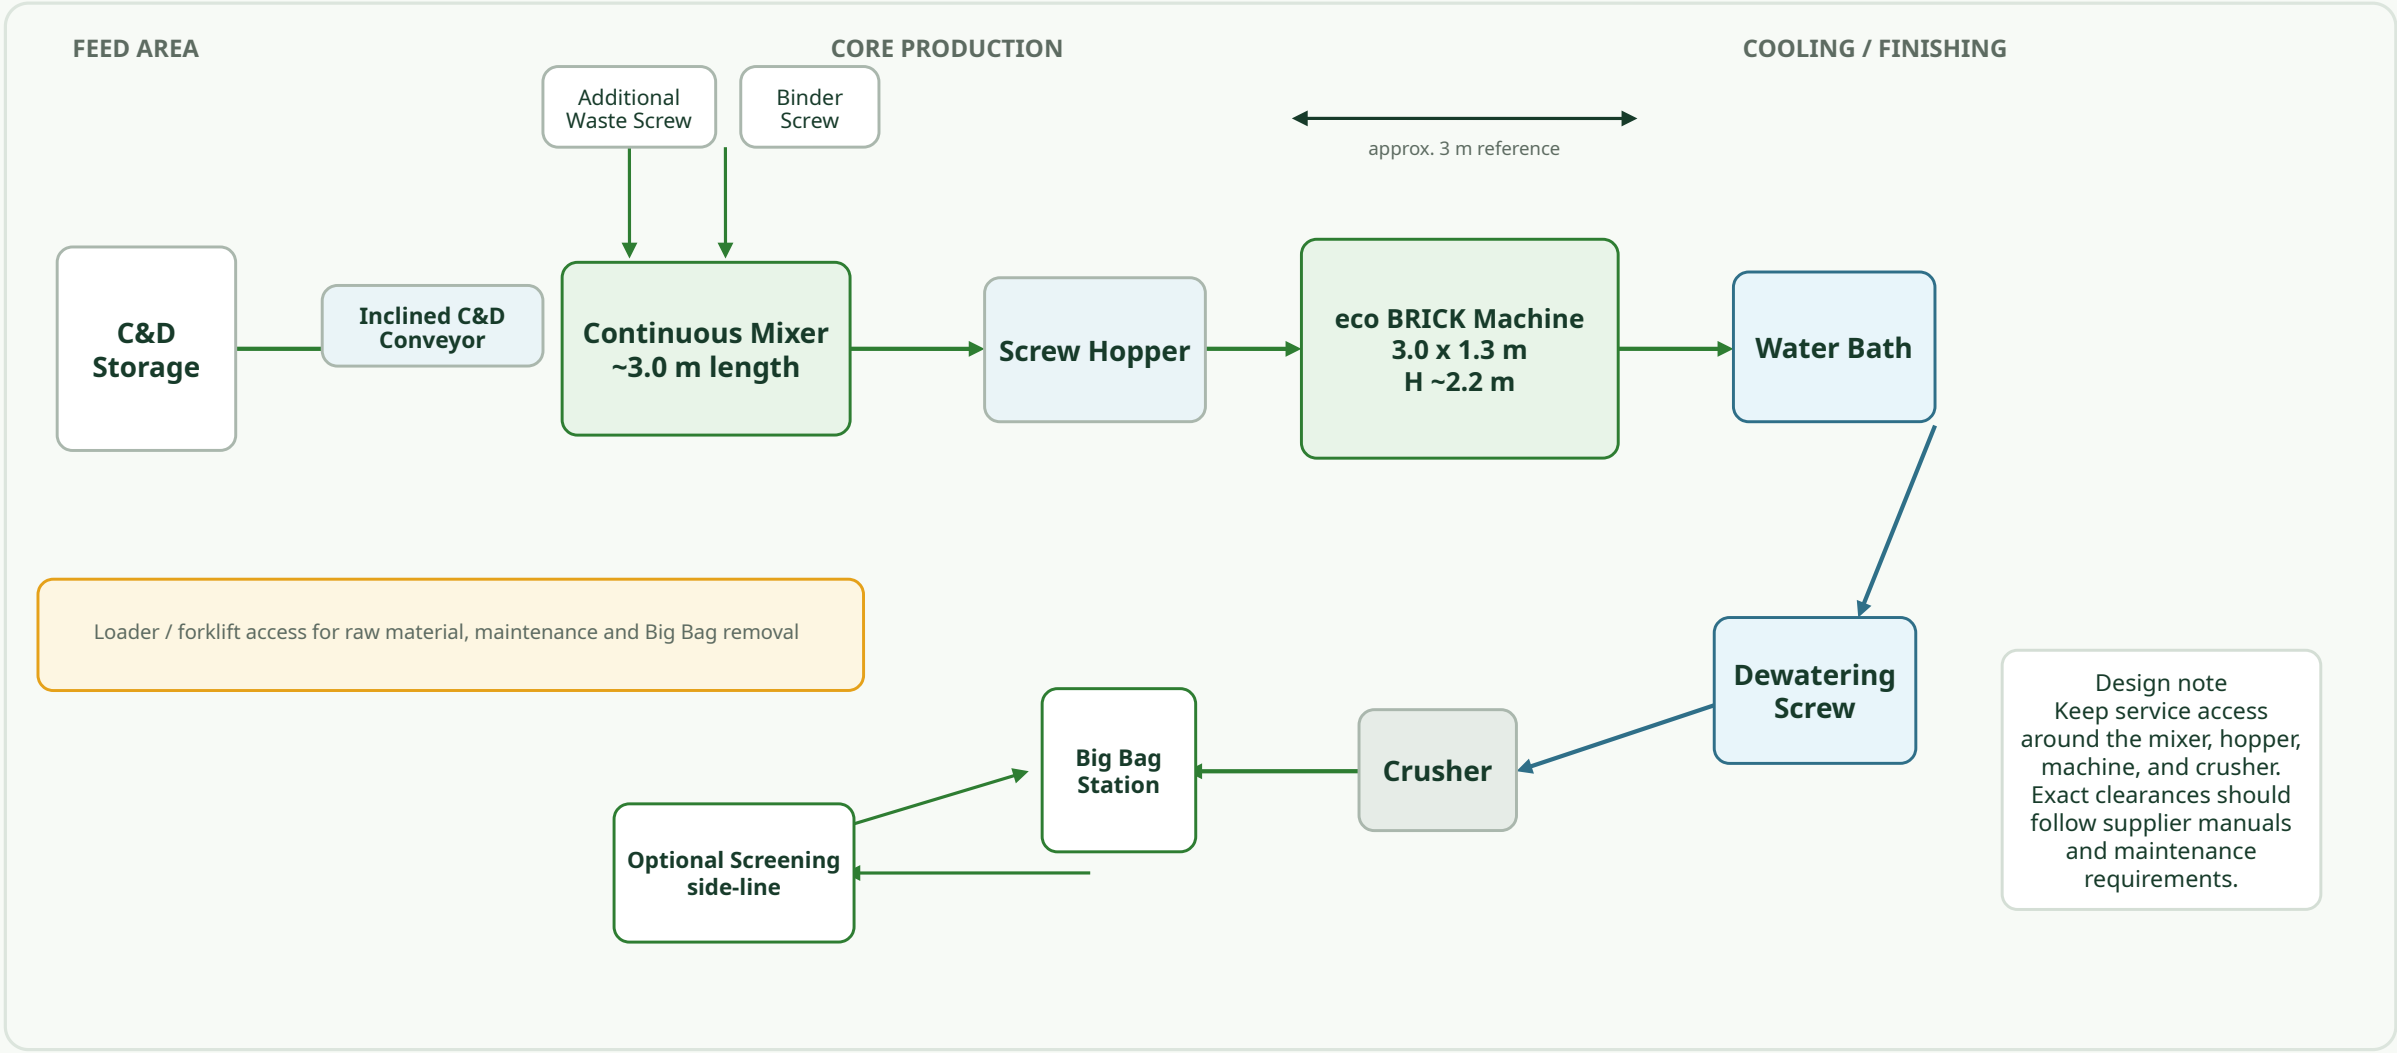

Conceptual engineering visualization - dimensions to be validated with equipment suppliers

3. What This Layout Enables Next

Use this deck as the visual base for equipment RFQs, supplier discussions, and site planning.

1. **Validate equipment dimensions**

   Mixer, screw feeds, hopper, water bath, dewatering screw, crusher, Big Bag frame.

2. **Set operating clearances**

   Maintenance openings, access to motors/bearings, crane/forklift access, safe walking paths.

3. **Confirm heights and gravity drops**

   Mixer to hopper, machine exit to water bath, dewatering screw to crusher, crusher to Big Bags.


4. **Define optional screening bypass**

   Required only for products that need exact fractions or customer-specific grading.

5. **Scale to multiple lines**

   The 3-machine layout should share raw material handling and finishing logistics wherever possible.

Core line summary

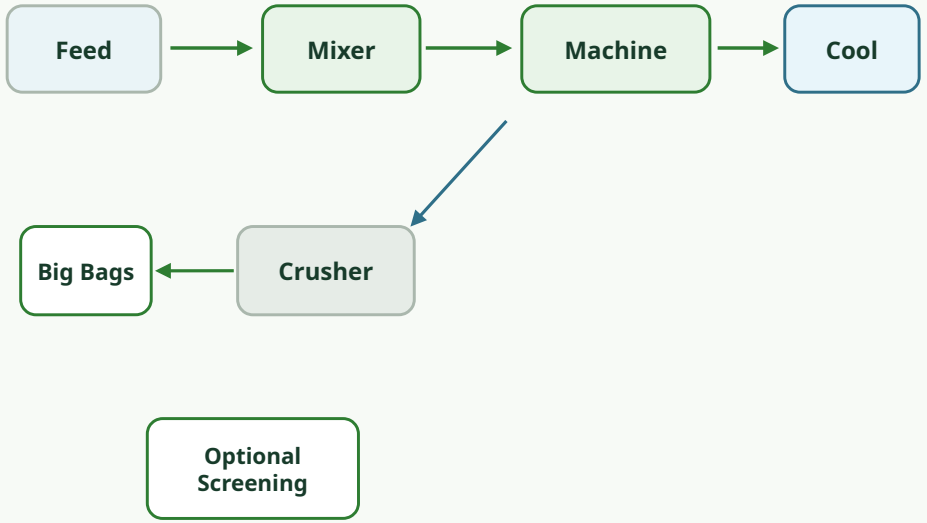

recommended deliverables after dimension validation:

- Scaled site plan
- Equipment RFQ diagram
- One-page investor process graphic
